



MONTHLY REPORT

UNIVERSITY OF RICHMOND
WELL-BEING CENTER & QUEALLY
ATHLETICS CENTER

MAY 2019

Barton Malow Company

Authored by: Kate Raivel

MAN HOURS AND SAFETY

MAN HOURS	RECORDABLE INCIDENTS
4004	0

TOP ACTIVITIES FOR APRIL

- Install of underground storm piping
- Install of underground sanitary piping
- Shotcrete and soil nail install at shoring wall
- Complete demolition of generator enclosure
- Cutting building pad to grade

CONTRACTORS ON SITE

CONTRACTOR	TRADE
ETEC	Mechanical & Plumbing
Commercial	Electrical
CT Purcell	Utilities & Earthwork
Stable Foundations	Shoring

UPDATED SCHEDULE

SEE ATTACHED SCHEULE


MAY AREAL PHOTO




PROGRESS PHOTOS




Cutting Building Pad to Grade

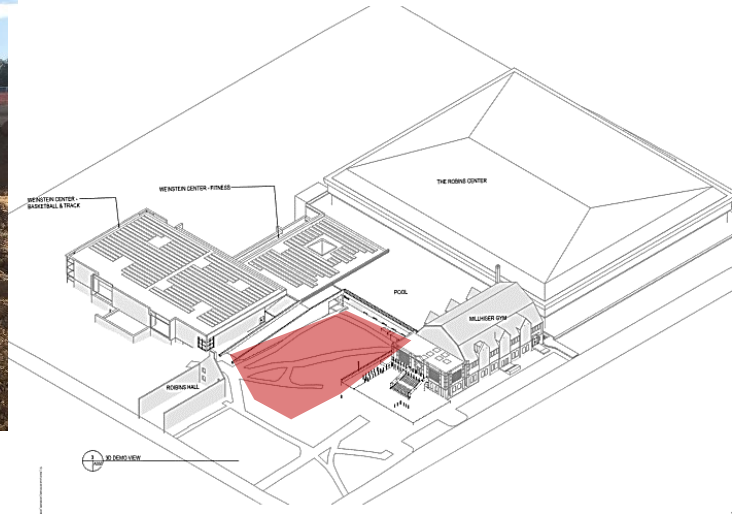


Storm Pipe Install

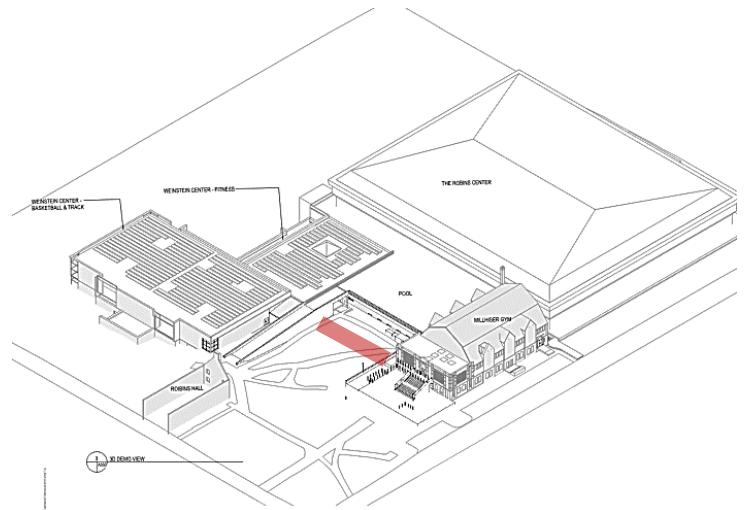


Detention Piping

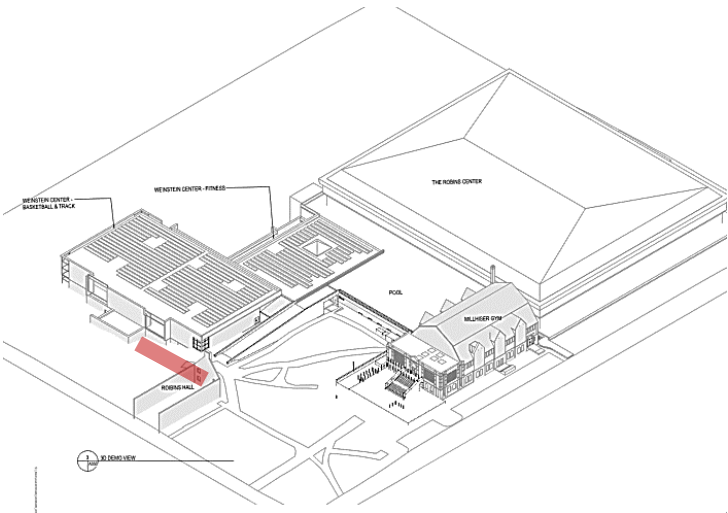


Shoring Wall

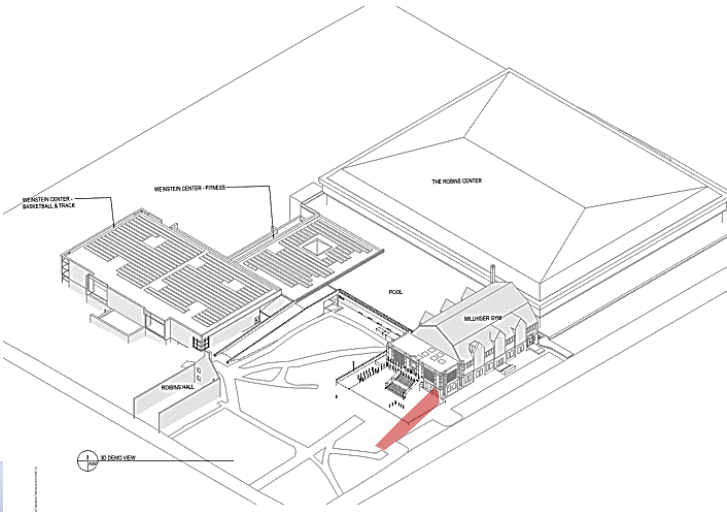


Excavation for Detention System

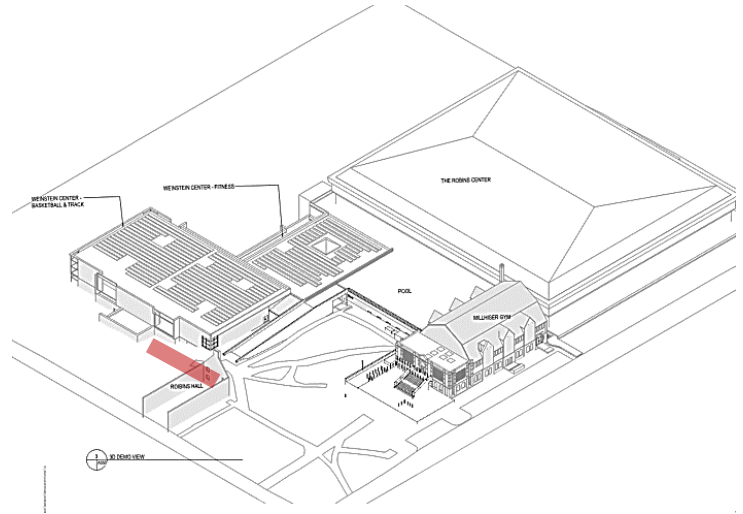


Demolition Complete at Generator Enclosure

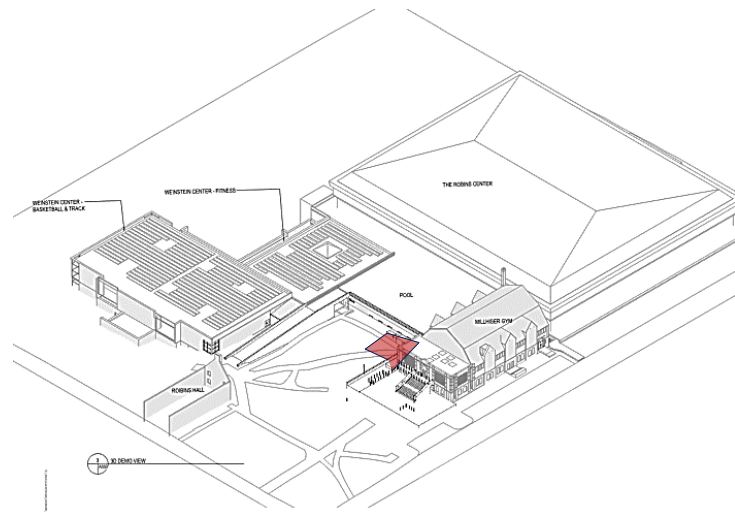

Soil Stock Pile

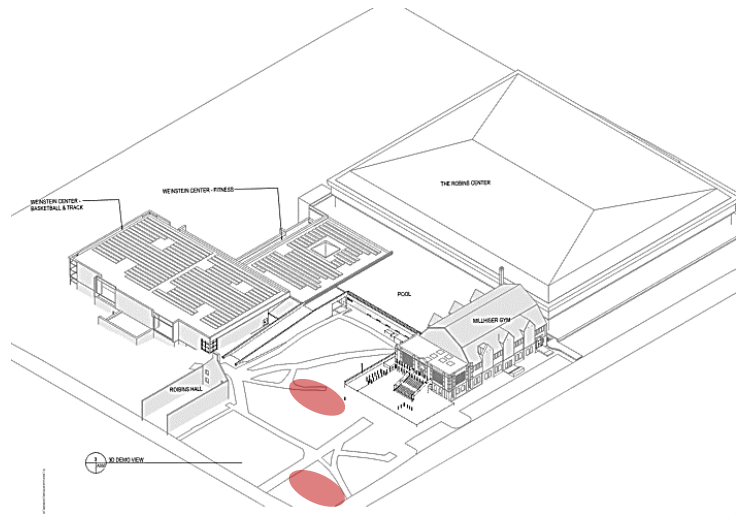

Brick and Mortar Mockup

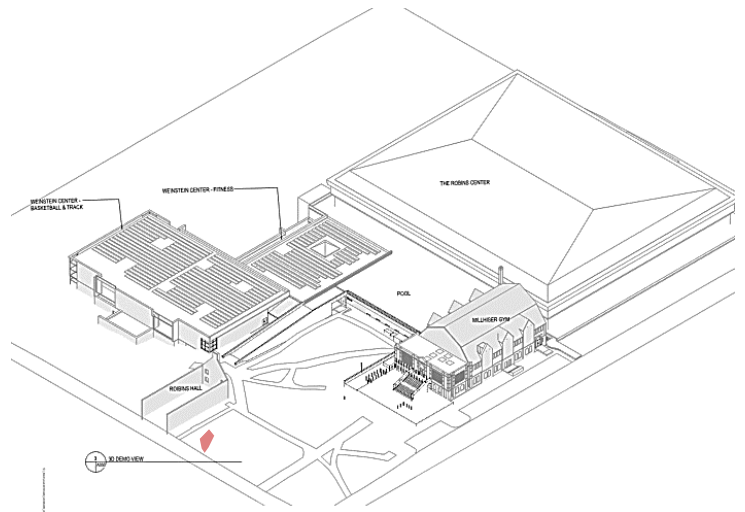

TOP ACTIVITIES FOR JUNE

- Begin pouring concrete foundations
- Helical piers installation
- Continue cutting building pad to grade
- Begin install of waterproofing
- Continue relocating storm sewer
- Continue relocating sanitary lines
- Underground MEP rough-in
- Form concrete cast in place walls
