



MONTHLY REPORT

UNIVERSITY OF RICHMOND
WELL-BEING CENTER & QUEALLY
ATHLETICS CENTER

JUNE 2019

Barton Malow Company

Authored by: Ethan Harrell

MAN HOURS AND SAFETY

MAN HOURS	RECORDABLE INCIDENTS
5400	0

TOP ACTIVITIES FOR JUNE

- Installation of Underground Storm Piping
- Installation of Underground Sanitary Piping
- Pouring Concrete Foundations
- Cutting Building Pad to Grade
- Installation of MEP Rough-In

CONTRACTORS ON SITE

CONTRACTOR	TRADE
ETEC	Mechanical & Plumbing
Commercial	Electrical
CT Purcell	Utilities & Earthwork
Stable Foundations	Shoring
Piedmont	Concrete

UPDATED SCHEDULE

SEE ATTACHED SCHEULE


AERIAL DRONE PHOTO




PROGRESS PHOTOS




Cutting Building Pad to Grade

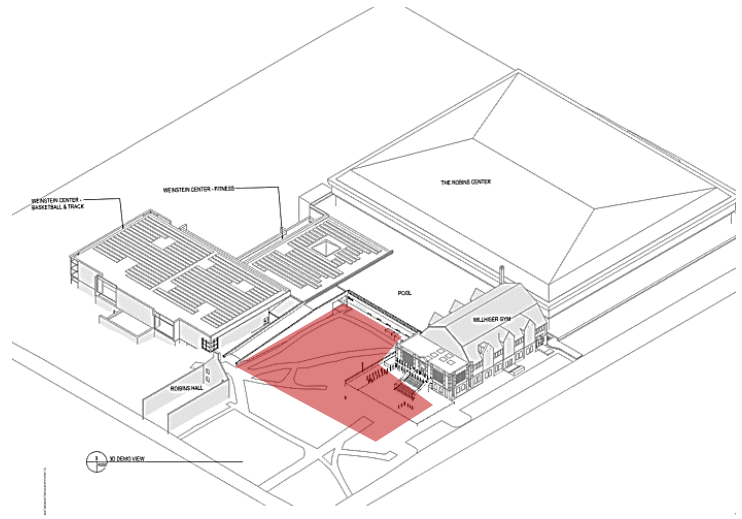


Foundation Work

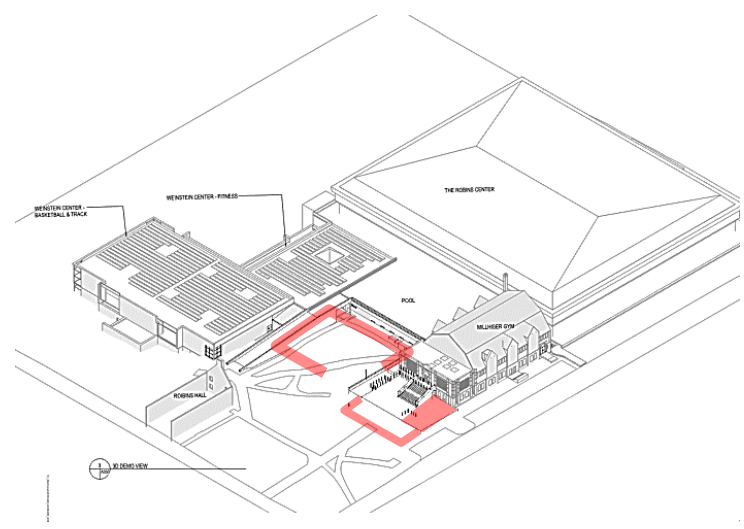

Detention Piping

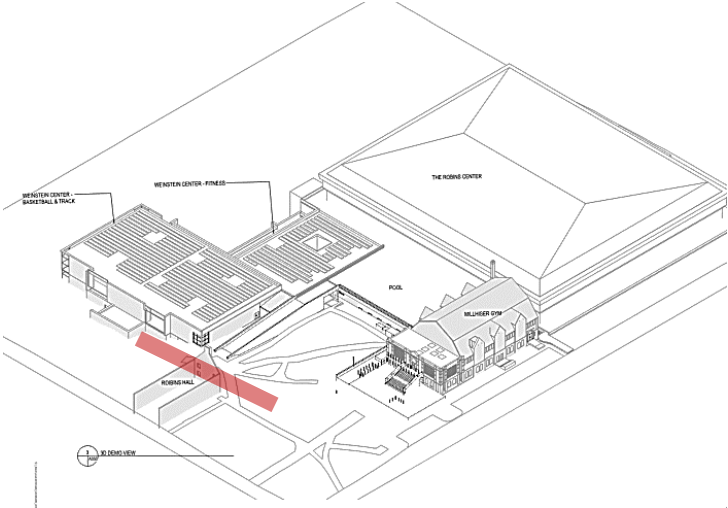


Hydropit Slab Foundation

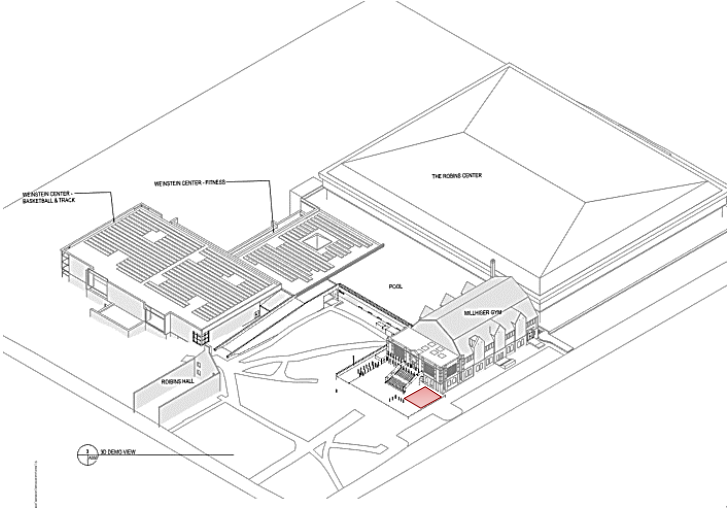




Excavation for Sanitary System

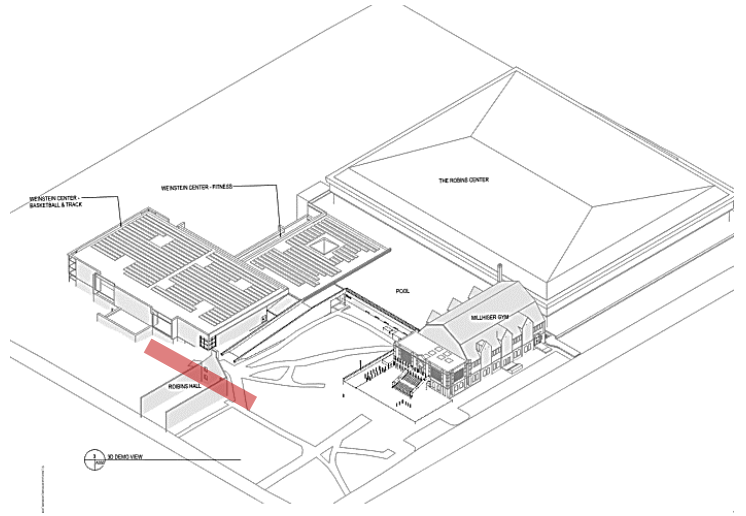

MEP Rough-In

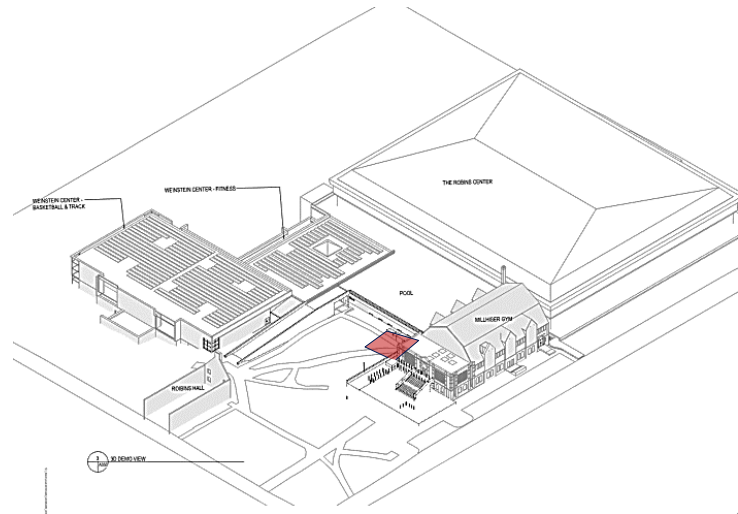

PULL PLANNING MEETING



TOP ACTIVITIES FOR JULY

- Complete Cutting Building Pad to Grade
- Complete Pouring Concrete Foundations
- Continue Installing Storm Sewer and Sanitary Lines
- Underground MEP Rough-in
- Form Cast-in-Place Concrete Walls
- CMU Foundation Walls
- Erecting Steel in Basketball Court and NW Corner
- Selective demolition in Millhiser
- Erecting Mezzanine Structural Steel in Millhiser
